


Jingle Bell 5K - Seattle

Measured by Tony Phillippi and Lori Giugler
 November 7, 2009 Seattle, WA
 lori@databarevents.com (206) 255-4044
NOT TO SCALE

Blow Up of Start & Finish

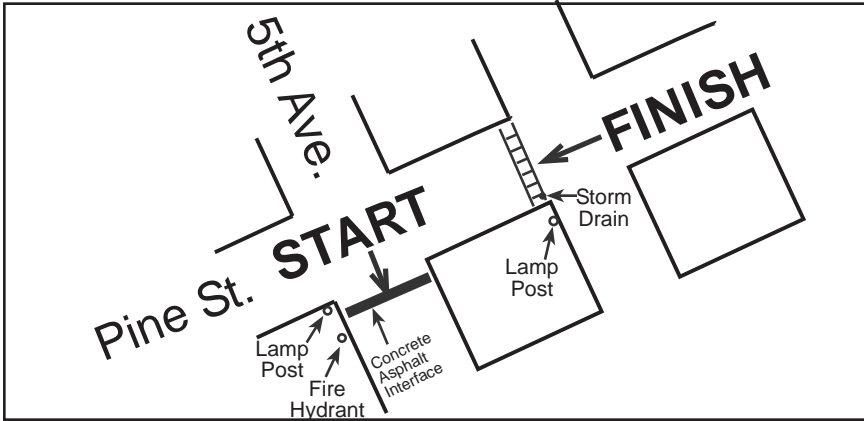

START: On 5th Ave, just south of Pine, at concrete/asphalt interface. Approx. 1.5 meters from fire hydrant and 2.6 meters from lamp post. Runners head Southeast. **500 meters:** On East side of 5th Ave, just South of YWCA entrance at 1118 5th Ave. **MILE 1:** In Express Lanes tunnel (entered via HOV entrance on 5th Ave.) and Columbia St.. Paint on Erigtside, 750 meters inside Express Lane tunnel. **MILE 2:** Going North of I-5 Express Lanes. Even with pier supporting I-5 Lanes. Paint is on East edge, 32.8 meters South of Turn Around. **TURN AROUND POINT:** Paint and nail in center of Express Lanes, 1.5 meters North of pier supporting I-5 Lanes and adjacent to Roy St. **MILE 3:** Paint on North side of Pine Street, 10 meters East of "15 Minute Charter Bus" sign and 20 meters East of lamp post #1314494. **FINISH:** Even with East edge of crosswalk and storm drain on West side of Pine St. and 6th Ave. intersection. Approximately 6.9 meters from lamp post on corner.

Blow Up of Turn Around

